

**Georgia Department of Public Health
ON-SITE SEWAGE MANAGEMENT SYSTEM INSPECTION REPORT**

CONSTRUCTION PERMIT NUMBER

454

COUNTY <i>Clarke</i>	COUNTY CODE <i>029</i>	HEALTH DISTRICT <i>010</i>	MONTH <i>06</i>	DAY <i>07</i>	YEAR <i>22</i>
SUBDIVISION:		LOT	PROPERTY OWNER: <i>Anthony Rader</i>		
PROPERTY LOCATION / ADDRESS: <i>925 Cleveland Rd</i>			SEWAGE CONTRACTOR: <i>Alan Leist</i>		
			CONTRACTOR LICENSE: <i>1P-16596 RCPST</i>		

ALL ITEMS: (BLANK) = Not Applicable (0) = Unknown *ITEMS (1) = Yes (2) = No


Section A - General	Section B - Primary / Pretreatment	Section C - Secondary Treatment
1. WATER SUPPLY: (1) Public (2) Private <i>well</i> <i>2</i> (3) Community	1. DISPOSAL METHOD: (1) Septic Tank (2) Privy (3) Aerobic Unit (4) Other:	1. ABSORPTION FIELD DESIGN <i>2</i> (1) Level (2) Serial (3) Drip (4) Bed (5) Distribution box (6) Mound (7) Other:
2. ** TYPE OF STRUCTURE: (see below)	2. SEPTIC TANK: a. Capacity (gals): <i>1000</i>	2. ABSORPTION FIELD: a. Total square feet: <i>600</i>
3. STRUCTURE AGE: (1) New (2) <1 year <i>3</i> (3) >1 year	b. Material: (1) Concrete (2) Polyethylene (3) Fiberglass (4) Poured (5) Other:	b. Total linear feet: <i>200</i>
4. SEWAGE SYSTEM: (1) New (2) Repair <i>2</i> (3) Addition	c. Distance from (feet): (1) Well: <i>100</i>	c. Number of trenches: <i>4</i>
5. AGE OF SYSTEM (repairs): (1) <1 (2) 1-5 (3) 6-10 (4) 11-20 (5) 21-30 (6) 31-40 (7) >40	(2) Building: <i>10</i>	d. Length trenches (feet): <i>48</i>
6. * IN SUBDIVISION?:	(3) Lake/Stream: <i>60</i>	e. Distance between trenches (feet): <i>17</i>
7. WATER USAGE BY: (1) Bedroom Numbers (2) Gallons per Day	(4) Nearest property line: <i>100</i>	f. Depth of trenches (range in inches): <i>24-36</i>
8. NO. OF BEDROOMS/ GALLONS PER DAY: <i>3</i>	d. Manufacturer: <i>McDaniel</i>	g. * Aggregate proper size:
9. LOT SIZE: <i>12</i>	3. FILTER MANUFACTURER/ MODEL: <i>TSS Hite</i>	h. * Aggregate proper depth:
10. PERCOLATION RATE/ LOADING RATE:	4. AEROBIC UNIT: a. Treatment capacity:	i. Distance from (feet): (1) Well: <i>600</i>
11. SOIL CLASSIFIER:	b. Manufacturer: <i>septic tank</i>	(2) Building: <i>500</i>
12. SOIL SERIES:	5. DOSING TANK CAP.(gals): <i>1000</i>	(3) Lake/Stream: <i>300</i>
	6. GREASE TRAP CAP.(gals):	(4) Nearest property line: <i>15</i>
		j. Nearest property line: (1) Right (2) Left <i>2</i> (3) Front (4) Rear
		k. Product used: <i>Quick 4 plus</i>

- ** TYPE OF FACILITY
- (1) Single-Family Residence
 - (2) Multi-Family Residence
 - (3) Commercial ≤2000
 - (4) Commercial ≥2000
 - (5) Restaurant
 - (6) Mobile Home Park
 - (7) Other (specify)

REMARKS:
26
57
50
4
20

Drawing not to scale.

Issuance of a construction permit for an on-site sewage management system, and subsequent approval of same by representatives of the County Board of Health shall not be construed as a guarantee that such systems will function satisfactorily for a given period of time; furthermore, said representatives do not, by any action taken in affecting compliance with these rules, assume any liability for damages which are caused, or which may be caused, by the malfunction of such system.

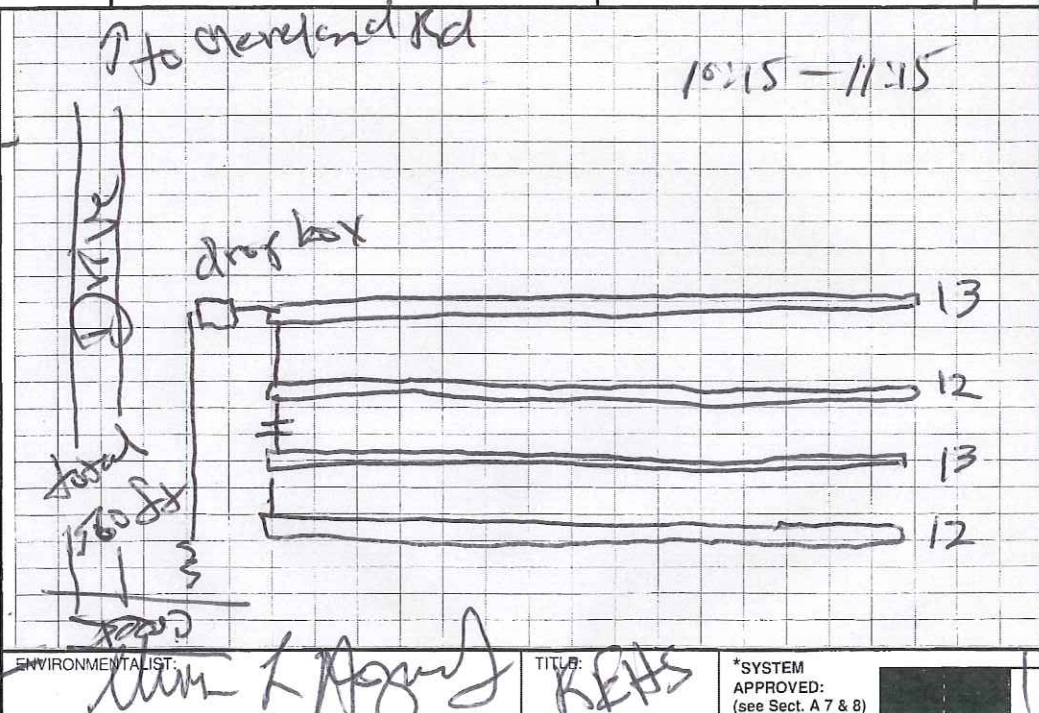

ENVIRONMENTALIST:

TITLE:

*SYSTEM APPROVED:
(see Sect. A 7 & 8)
